




40.017/Lynch Mission Schedule

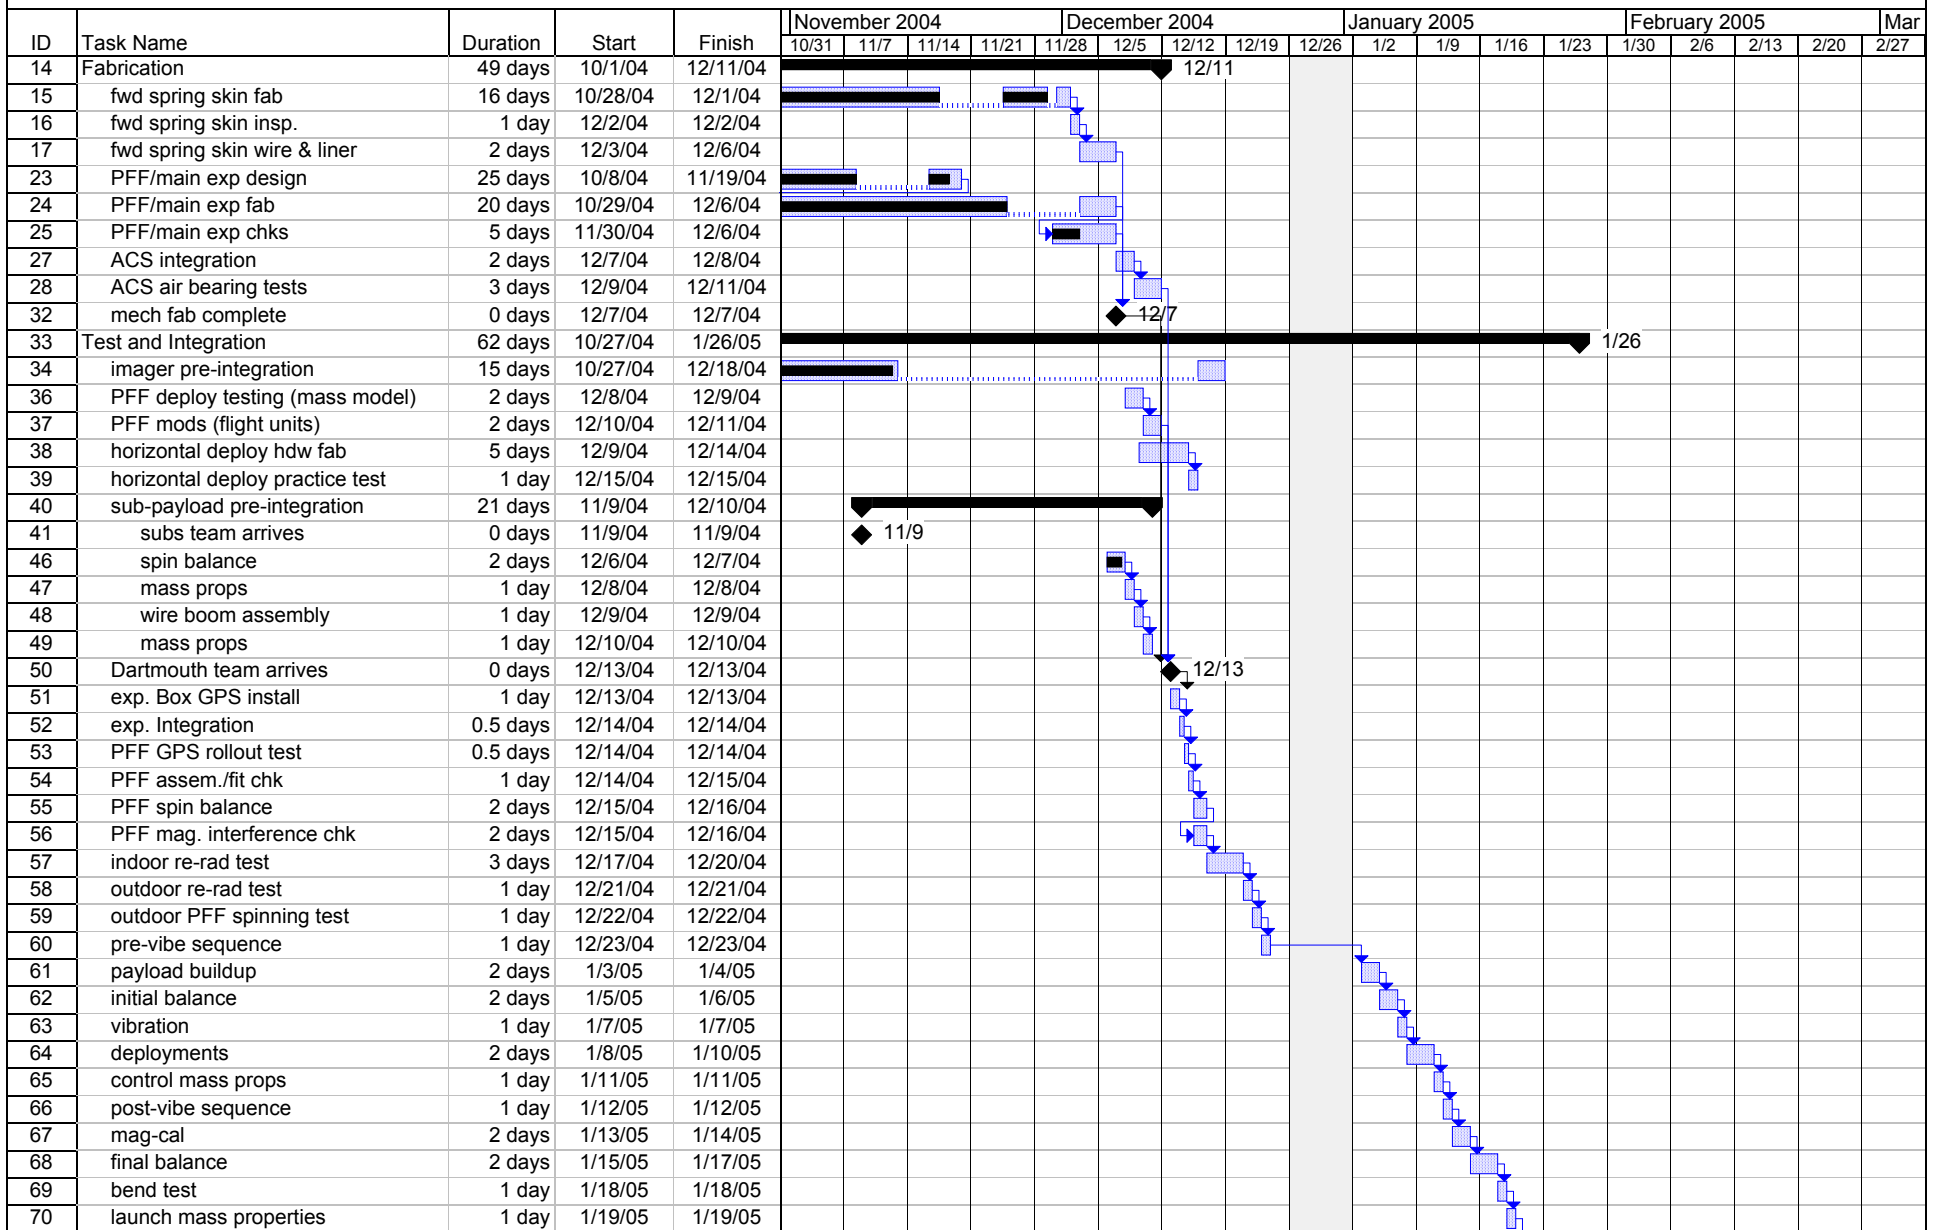

40.017/Lynch Mission Schedule

ID	Task Name	Duration	Start	Finish	November 2004				December 2004				January 2005				February 2005				Mar	
					10/31	11/7	11/14	11/21	11/28	12/5	12/12	12/19	12/26	1/2	1/9	1/16	1/23	1/30	2/6	2/13	2/20	2/27
71	ACS final air bearing	5 days	1/20/05	1/26/05																		
72	corona test	1 day	1/20/05	1/20/05																		
73	post-vibe TM chks	3 days	1/20/05	1/24/05																		
74	MRR	1 day	1/27/05	1/27/05																		
75	pack	2 days	1/31/05	2/1/05																		
76	shipping	4 edays	2/2/05	2/6/05																		
77	Field Operations	15 days	2/6/05	2/25/05																		
78	NSROC Team Travels	1 eday	2/6/05	2/7/05																		
79	payload test & assem.	15 days	2/7/05	2/25/05																		
80	Launch Window	15 edays	2/27/05	3/14/05																		
81	NSROC team return travel	1 day	3/16/05	3/16/05																		
82	mission closeout	90 edays	3/16/05	6/14/05																		
83	TMCR due	0 days	6/14/05	6/14/05																		



12/7/04

Task		Milestone		Rolled Up Split		External Tasks		Deadline	
Split		Summary		Rolled Up Milestone		Project Summary			
Progress		Rolled Up Task		Rolled Up Progress		External Milestone			
